

LAB 2

Agile Backlog Creation & Sprint Simulation in Jira

Multi-Cloud Asset Cost Optimization Portal

Student	R Vinay
SRN	PES1UG24CS353
Section	F
Problem Statement	45 - Multi-Cloud Asset Cost Optimization Portal
Jira Space	Multi-Cloud Asset Cost Optimization Portal
Sprint completed	SCRUM Sprint 1

Purpose

This report records the Jira backlog, user-story estimates, Sprint 1 execution, and the Burndown Chart for the Multi-Cloud Asset Cost Optimization Portal. The backlog was derived from the functional requirements and use cases prepared in Lab 1.

Scope note: one sprint was completed, in line with the instructor instruction used for the submission.

1. Backlog structure

The Lab 1 functional requirements were converted into four Jira Epics. Related User Stories were placed under those Epics, assigned priorities, and estimated using Fibonacci-style story points.

Lab 1 item	Jira Epic	User Story / Stories
FR-001 - ingest billing data and categorize cloud costs	SCRUM-5 - Multi-Cloud Billing & Cost Analysis	SCRUM-9 Ingest Cloud Billing Data; SCRUM-10 Categorize Cloud Costs
FR-002 - identify idle compute	SCRUM-6 - Idle & Unattached Asset Detection	SCRUM-11 Detect Idle Compute
FR-003 - identify unattached storage	SCRUM-6 - Idle & Unattached Asset Detection	SCRUM-12 Detect Unattached Storage
FR-004 - define budget threshold	SCRUM-7 - Budget Monitoring & Alerts	SCRUM-13 Set Budget Thresholds
FR-005 - dispatch budget breach alert	SCRUM-7 - Budget Monitoring & Alerts	SCRUM-14 Trigger Budget Alerts
UC-06 - Resolve Flagged Asset	SCRUM-8 - Asset Resolution & Audit	SCRUM-15 Resolve Flagged Asset
UC-07 - Add Resolution Note	SCRUM-8 - Asset Resolution & Audit	SCRUM-16 Add Resolution Note

Epic summary

Epic	Description
SCRUM-5 - Multi-Cloud Billing & Cost Analysis	Ingest AWS, Azure, and GCP billing data and categorize cloud costs by service type and project tag.
SCRUM-6 - Idle & Unattached Asset Detection	Identify idle compute instances and unattached storage resources to locate potential cost savings.
SCRUM-7 - Budget Monitoring & Alerts	Define monthly budget thresholds and notify administrators when spending exceeds configured limits.
SCRUM-8 - Asset Resolution & Audit	Resolve flagged resources and record resolution or exclusion information for audit purposes.

User stories and estimates

Key	Summary	Parent	Priority	Points
SCRUM-9	Ingest Cloud Billing Data	SCRUM-5	High	8
SCRUM-10	Categorize Cloud Costs	SCRUM-5	High	5
SCRUM-11	Detect Idle Compute	SCRUM-6	High	8
SCRUM-12	Detect Unattached Storage	SCRUM-6	High	5
SCRUM-13	Set Budget Thresholds	SCRUM-7	High	5
SCRUM-14	Trigger Budget Alerts	SCRUM-7	High	5
SCRUM-15	Resolve Flagged Asset	SCRUM-8	High	8
SCRUM-16	Add Resolution Note	SCRUM-8	Medium	3
				47 total

The story descriptions used the requested end-user format: “As a [role], I want [goal], so that [benefit].” Story points were 3, 5, or 8, with a total sprint estimate of 47 points.

2. Sprint 1 evidence

The Jira board was used to move the planned stories through the Scrum workflow during the simulation. The checkpoints below record the observed board states.

Checkpoint	Done	In Progress	To Do
Checkpoint 1	2	2	4
Checkpoint 2	6	0	2
Final	8	0	0

Checkpoint 1

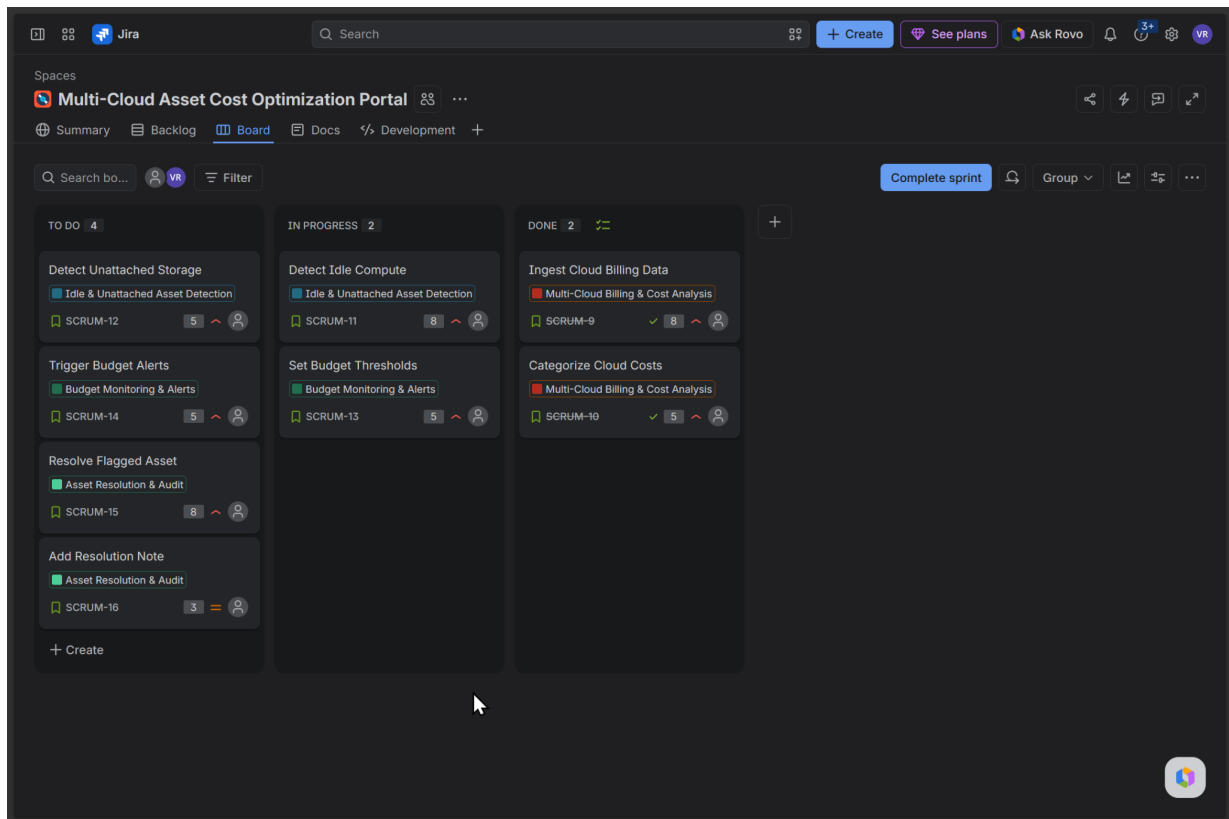


Figure 1. Jira board checkpoint: 2 stories Done, 2 In Progress, and 4 To Do.

3. Final Sprint 1 state

The second checkpoint shows six completed stories with two still to do. The final board state below shows all eight User Stories in Done, with no work remaining in To Do or In Progress.

Checkpoint 2

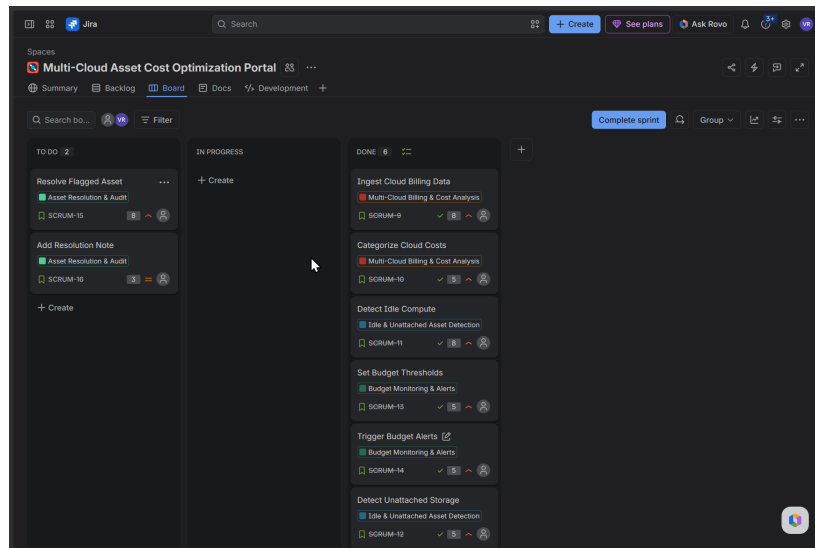


Figure 2. Jira board checkpoint: 6 stories Done and 2 To Do.

Final state

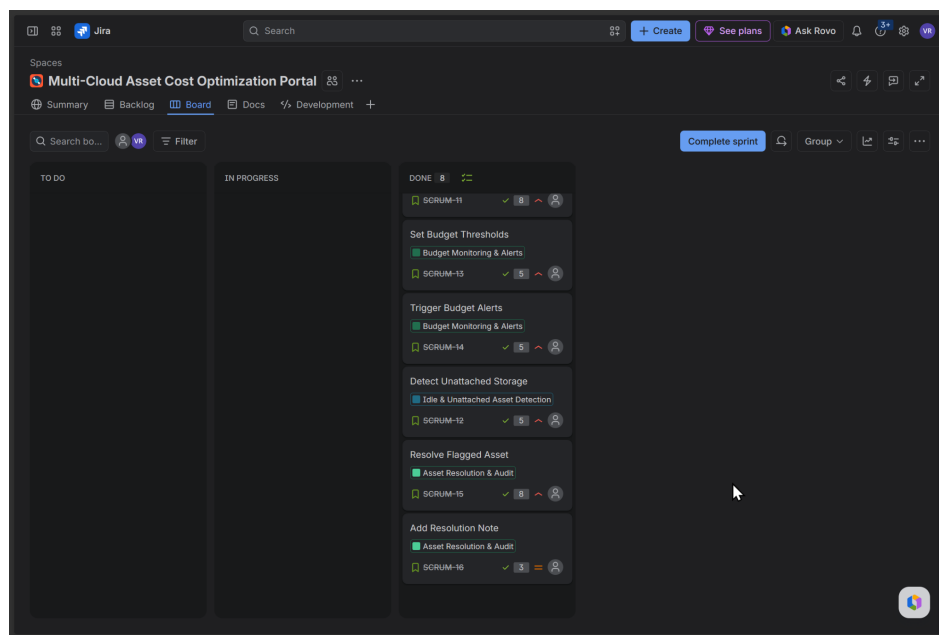


Figure 3. Completed Sprint 1 board: 8 stories in Done, 0 in To Do, 0 In Progress.

Completion summary

Measure	Result
Stories completed	8 of 8
Story points completed	47 of 47
Final status	All stories Done
Second sprint	Not run - instructor directed one sprint

The Jira sprint was completed after all eight stories were moved through the workflow.

4. Burndown Chart

The Burndown Chart below is the actual Jira report for SCRUM Sprint 1 with Story points selected as the estimation field. The sprint began with 47 remaining points and ended at 0.

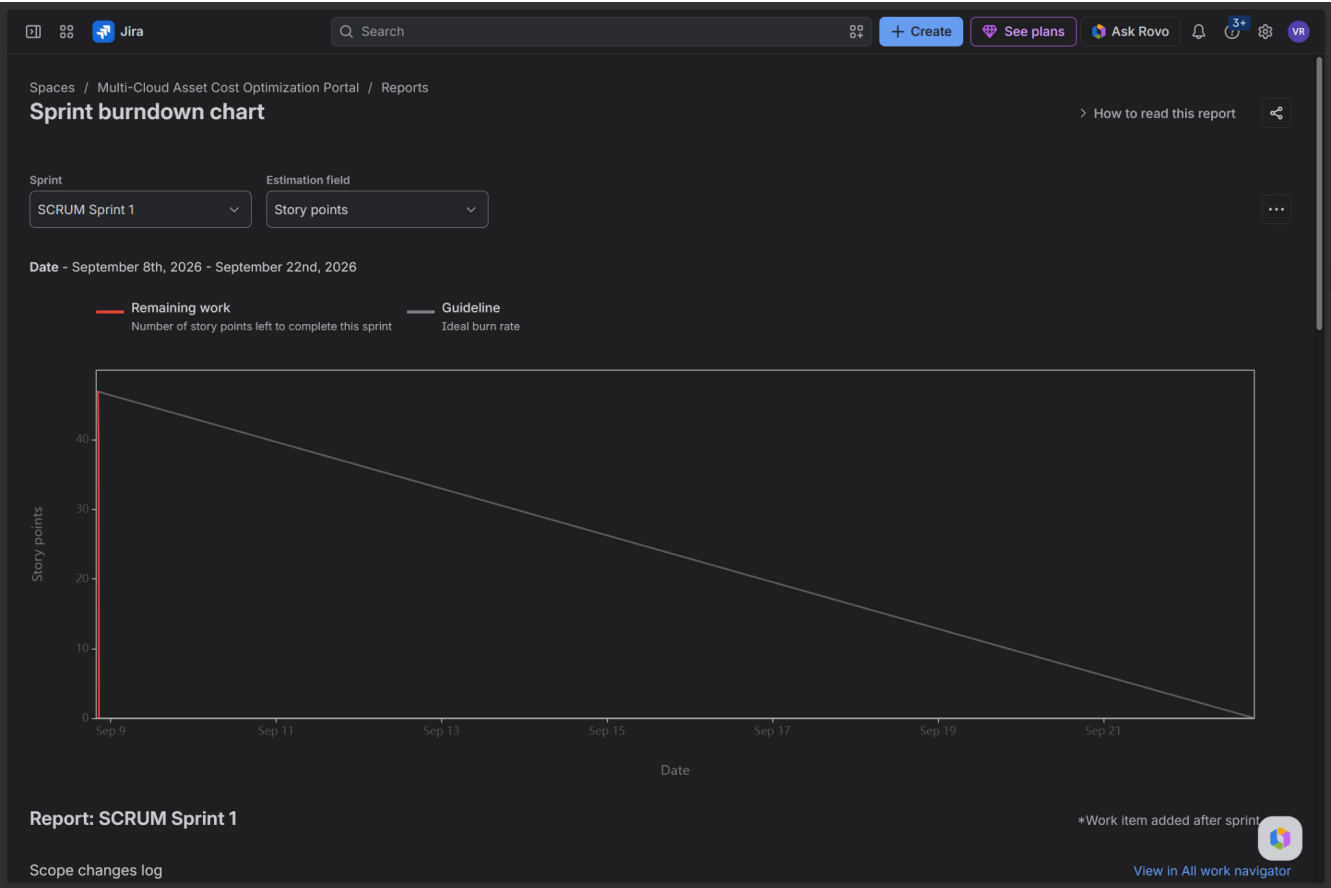


Figure 4. Actual Jira Sprint burndown chart for SCRUM Sprint 1.

Interpretation

The gray guideline represents the ideal linear burn rate. The red Remaining work line records the actual points left to complete. In this simulated sprint the work dropped to zero by completion, indicating that the full planned scope was delivered. Because the sprint was executed as a simulation, the chart should be read as evidence of sprint completion rather than as a long-term measure of sustainable team velocity.

Sprint data

Field	Value
Sprint	SCRUM Sprint 1
Estimation field	Story points
Date shown in Jira	September 8, 2026 - September 22, 2026
Starting remaining work	47 points
Ending remaining work	0 points

5. Reflection

1. Did your estimations reflect the actual effort?

Yes. The eight stories were estimated with Fibonacci-style values of 3, 5, and 8 points, giving a total of 47 points. All 47 points were completed. Since this was a simulated sprint rather than actual product development, the estimates are best understood as relative measures of complexity, effort, and uncertainty.

2. Was your backlog well-prioritized?

Yes. The core billing, cost analysis, idle-resource detection, budgeting, and alerting stories were assigned High priority. The resolution-note story was assigned Medium because it supports the workflow and audit trail rather than the primary cost-optimization function.

3. How did your simulated sprint align with your plan?

The sprint aligned with the planned scope. All eight selected stories were moved through To Do, In Progress, and Done. The planned scope was 47 points, and all 47 points were completed in Sprint 1.

4. What insights did the burndown chart give about your team's capacity?

The chart shows a complete burn from 47 points remaining to 0. This indicates that the planned sprint scope was completed. However, because the sprint was deliberately simulated in a short period, the result should not be used as a reliable long-term velocity or capacity benchmark.

6. Submission checklist

Requirement	Status
Jira Epics and User Stories	Complete
Story point assignments	Complete - 47 points
Active Sprint evidence	Included
Sprint 1 progress/completion evidence	Included
Burndown Chart	Included - 47 to 0 points
Reflection questions	Answered
Second sprint	Not run - instructor direction was one sprint

Accuracy note: Jira showed Sprint 1 dates of September 8, 2026 to September 22, 2026 (2 weeks). The Lab 2 handout text specifies a 1-week sprint. The report records the Jira dates actually shown during execution rather than altering the evidence.
